


ID	Task Mode	WBS	Nombre de tarea	Duration	Finish	020	Qtr 1, 2021	Qtr 2, 2021	Qtr 3, 2021	Qtr 4, 2021	Qtr 1, 2022	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023
0		0	REMOZAMIENTO PALACIO DE JUSTICIA SANTIAGO	140 days	Fri 10/15/21	140 days										
1		1	REMOZAMIENTO PALACIO SANTIAGO	140 days	Fri 10/15/21	140 days										
2		1.1	Planificación preliminar (CONTRATISTA)	3 days	Wed 4/7/21	3 days										
3		1.2	Inicio suministro de materiales San Pedro	0 days	Mon 4/5/21	0 days										
4		1.3	Suministro de materiales	40 days	Wed 6/2/21	40 days										
5		1.4	Fin Suministro de materiales	0 days	Wed 6/2/21	0 days										
6		1.5	Ejecución de Obra	135 days	Wed 10/13/21	135 days										
7		1.3.5	Baños publicos del sotano damas y caballeros	45 days	Wed 6/9/21	45 days										
8		1.5.2	Baños publicos primer nivel de damas y caballeros	30 days	Wed 7/21/21	30 days										
9		1.5.3	Baños publicos del segundo nivel damas y caballeros	30 days	Wed 9/1/21	30 days										
10		1.5.4	Accesibilidad (2 Rampas frontales)	25 days	Wed 5/12/21	25 days										
11		1.5.5	Miscelaneos primer nivel	30 days	Wed 10/13/21	30 days										
12		1.5.6	Baños publicos tercer nivel de damas y caballeros	20 days	Wed 7/7/21	20 days										
13		1.5.7	Miscelaneos	30 days	Wed 8/18/21	30 days										
14		1.6	Recepción final de obra	2 days	Fri 10/15/21	2 days										
15		1.7	Finalización de obra	0 days	Fri 10/15/21	0 days										

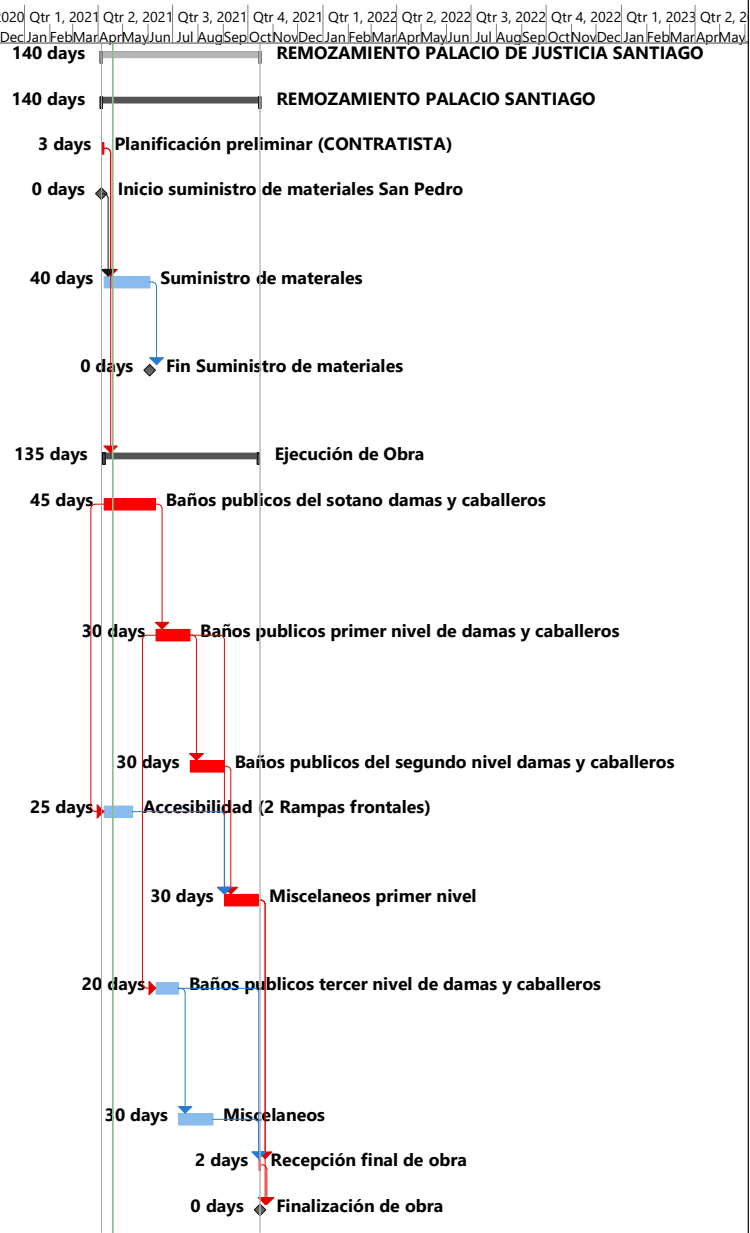

Proyecto: REMOZAMIENTO PA  
 Fecha: Mon 4/19/21

Task		Project Summary		Rolled Up Progress		Inactive Summary		Start-only	
Task Progress		Group By Summary		External Tasks		Manual Task		Finish-only	
Split		Rolled Up Task		External Milestone		Duration-only		Deadline	
Milestone		Rolled Up Critical Task		Inactive Task		Manual Summary Rollup		Critical Task	
Summary		Rolled Up Milestone		Inactive Milestone		Manual Summary		Critical Task Progress	
